# Phoenix Environmental Safety Ltd.

## **ASBESTOS SURVEY REPORT**

(Refurbishment / Demolition Survey)

Client: Longford County Council, Aras an Chontae, Great Water Street, Longford

> Location: No. 24 Congress Terrace, Longford Town, Co. Longford

> > Date: 25th May 2021

Report No. PE21-457



Graigueswood, Freshford, Co. Kilkenny

Tel: 056 8832414 Fax: 056 8832950 admin@phoenixenv.ie www.phoenixenv.ie

Client: Longford County Council, Aras an Chontae, Great Water Street, Longford

Location: No. 24 Congress Terrace, Longford Town, Co. Longford

Asbestos Survey Type: Refurbishment/Demolition Asbestos Survey

Survey Company: Phoenix Environmental Safety Ltd.

Surveyors: John Hickey

Testing Laboratory: Phoenix Environmental Safety Ltd.

Date of Survey: 21st May 2021

Date of Survey Report: 25th May 2021

Report issue: Final

Signed: John Hickey Date: 25th May 2021

This report cannot be used for contractual or engineering purposes unless this sheet is signed where indicated by Surveyor. The report must also be designated 'final' on the signatory sheet.

Please note that Phoenix Environmental Safety Ltd. cannot be held responsible for the way in which the Client interprets or acts upon the results. The report must be read in its entirety including any appendices. Phoenix Environmental Safety Ltd. accepts no responsibility for sub-division of this report. All measurements in this report are approximate and therefore should not be used by the asbestos removal contractor for pricing purposes. The asbestos removal contractors should ascertain for themselves, by site measurements and inspection, the exact nature and extent of the work to be done.

The survey information should be used to help in the tendering process for removal of ACMs from the building before work starts. The survey report should be supplied by the client to designers and contractors who may be bidding for the work, so that the asbestos risks can be addressed. In this type of survey, where the asbestos is identified so that it can be removed (rather than to manage it), the survey does not normally assess the condition of the asbestos, other than to indicate areas of damage or where additional asbestos debris may be present. However, where the asbestos removal may not take place for some time, the ACMs' condition will need to be assessed and the materials managed.

TABLE OF CONTENTS	PAGE
Cover sheet	1
Signatory Sheet	2
Table of Contents	3
Summary	4
Introduction	5-6
Appendix A (Asbestos materials in buildings)	7-8
Appendix B (Results of Laboratory Analysis)	9-10
Appendix C (Asbestos Data Sheets)	11-13
Appendix D (Non asbestos containing materials)	14-16
Appendix E (Non-accessible locations)	17
Appendix F (Floor plans & location of asbestos containing materials)	18-19

#### **SUMMARY**

Following a request made by Sweeney Architects, we have produced this Refurbishment/Demolition Asbestos Survey report for No. 24 Congress Terrace, Longford Town with the aim of finding asbestos containing materials (ACMs) within the scope of the asbestos survey.

The scope of the asbestos survey was confined to all accessible areas of the existing dwelling at No. 24 Congress Terrace which is due for major refurbishment works.

During the asbestos survey at No. 24 Congress Terrace, the following asbestos containing materials were detected in the following locations:

- An asbestos containing toilet cistern was identified in the W/C on the ground floor
- Asbestos containing bitumen adhesive was identified in the ground floor entrance porch, kitchen and front room (35 m² approx.)

See Appendix C & F for more details

#### INTRODUCTION

#### **Background**

Asbestos has been used extensively in the building industry for over one hundred years and has proved to be an excellent product for a variety of uses, having many qualities such as insulation, fire and chemical resistance to name a few. Its suitability across a wide range of uses and its relatively cheap cost made it very popular, with over 3,000 different asbestos products having been recorded.

The use of asbestos containing materials (ACM's) was most prevalent between the 1950's and 1970's when it provided an economic, easy to use and versatile material. Unfortunately, given the constitution and make up of asbestos it can give rise to microscopic airborne fibres being released into the working environment. The fibres have carcinogenic properties caused by inhalation of the fibres which can get lodged in the lining of the lungs causing disease and death.

#### Scope & Purpose

Longford County Council have commissioned Phoenix Environmental Safety Ltd. to undertake an asbestos survey at No. 24 Congress Terrace, Longford Town. The aim of the survey was to locate and identify the presence of asbestos containing materials (ACM's) or suspected ACM's within the scope of the asbestos survey. This report provides a record and assessment of the extent and characteristics of ACM's and is based on information made available on the 21st May 2021.

This particular survey comprised of a standard Refurbishment/Demolition Survey carried out in accordance with S.I. No. 386 of 2006 Safety, Health and Welfare at Work (Exposure to Asbestos) Regulations 2006-2010 and with the guidance contained in The Health and Safety Authority's guidance document: Asbestos Containing Materials (ACMs) in Workplaces - Practical Guidelines on ACM Management & Abatement (2013), The Health and Safety Executive's (UK) guidance documents HSG 264 (Asbestos: The Survey Guide) and HSG 227 (A Comprehensive Guide to managing Asbestos in Premises).

#### This means that:

- As far as reasonably practicable, locate and describe all ACM's in all reasonably accessible areas within the scope of the survey
- A sampling programme is undertaken to identify possible ACM's and estimates of the volumes and the surface areas of ACM made
- A record of the condition of the ACM's or where additional asbestos debris may be expected to be present is produced

#### Refurbishment / Demolition Surveys (formerly type 3 surveys)

This type of survey is necessary prior to any refurbishment (including "minor") or demolition work being carried out. These "refurbishment / demolition" surveys will be much more intrusive and destructive compared with management surveys as their intention is to locate all the ACMs so that they can be removed before the refurbishment or demolition takes place. Refurbishment/demolition surveys are required as necessary when the needs or use of the building changes and the fabric of the building will be disturbed or complex fixed plant and equipment are to be dismantled.

#### The purpose of the report is to:

- Enable the client to take appropriate precautions so that people who work at No. 24 Congress Terrace during the forthcoming refurbishment works are not exposed to asbestos-related health risks
- Provide information to assist the client in developing and implementing an action plan before any refurbishment works or demolition is carried out

#### **Presentation of Findings**

#### **Data Sheets**

A series of data sheets have been prepared to provide assessments and recommendations for each of the locations where samples were taken. These data sheets are presented in Appendix C.

#### **Figures**

The schematic diagrams presented in Appendix F at the rear of this document shows the locations of all of the asbestos containing materials detected during the asbestos survey.

#### Caveats

All reasonable steps have been taken to ensure that the contents and findings of this report are true and accurate. Though as stated below, further undetected ACM's may still be present within the premises. The client should therefore be aware of his responsibilities for identifying, locating, removing and/or managing all ACM's within the premises, and for notifying the appropriate authorities where necessary.

#### **Refurbishment / Demolition Surveys**

This type of survey employs the use of destructive sampling techniques of an unfamiliar site. Although every effort is made to locate all asbestos containing materials, it is impossible to rule out the possibility that undiscovered asbestos materials may be present. If the building is to undergo major refurbishment or demolition, it is recommended that the persons carrying out the work are made aware of this and take sufficient precautions, as may be appropriate, to ensure the health and safety of their own employees and any other parties who may be affected by the works.

## **APPENDIX A**

#### **ASBESTOS MATERIALS IN BUILDINGS**

**Sprayed coatings** applied in Ireland were typically a mixture of hydrated asbestos cement containing up to 85% asbestos, mainly amosite but crocidolite and mixtures have been used. Primarily used for anti-condensation and acoustic control and fire protection to structural steelwork. It is a friable material but if in a good condition and unlikely to be disturbed presents no immediate danger; however it is likely to release fibres, if disturbed especially during repair and maintenance work. As it ages the binding medium of sprayed asbestos may degrade with the consequent release of more fibres.

**Thermal insulation** to boilers, vessels, pipe work, valves, pumps etc also known as hand applied lagging. Lagging may have a protective covering of cloth, tape, paper, metal or a surface coating of cement. All types of asbestos may be found in lagging and the content can vary between 15 and 85% asbestos with the protective papers being up to 100% chrysotile. The likelihood of fibre release depends upon its composition, friability and state of repair, but it is particularly susceptible to damage and disturbance through maintenance work or the action of water leaks.

**Asbestos insulating boards** usually contain between 15 to 40% amosite, although boards may be found to contain other types of asbestos and in other quantities. Insulating boards were developed in the 1950s to provide an economical, lightweight, fire resisting insulating material. As insulation board is semi-compressed it is more likely to release fibres as a result of damage or abrasion. Work on asbestos insulation board can give rise to high levels of asbestos fibre.

**Asbestos cement products** as in roofing slates, wall cladding, permanent shuttering, flue, rain water and vent pipes generally contain 10 to 15% of asbestos fibre bounded in Portland cement, some flexible boards contain a small proportion of cellulose. All three types of asbestos have been used in the manufacture of asbestos cement. The asbestos fibres in asbestos cement are usually firmly bound in the cement matrix and will be released only if the material is mechanically damaged or as it deteriorates with age.

Ropes and yarns are usually high in asbestos content, approaching 100% and all three types of asbestos have been used in their manufacture. They were used as in the pipe lagging process and in pipe jointing and also for packing materials as in heat/fire resistant boiler, oven and flue sealing or anywhere thermal of fire protection was required. The risk of fibre release depends upon the structure of the material; bonded gasket material is unlikely to release asbestos but an unbonded woven material may give rise to high fibre release especially if when damaged or frayed.

**Cloth thermal insulation and lagging**, including fire resistant blankets, mattresses and protective curtains, gloves, aprons, overalls etc. All types of asbestos have been used in the manufacture but since the mid 60's the majority has been chrysotile, the content of which can be up to 100 %.

**Millboard, paper and CAF gaskets** usually have an asbestos content approaching 100% with all three types of asbestos being used in their manufacture. They were used for insulation of electrical equipment and for thermal insulation. Asbestos paper has been used as a laminate for fireproofing to various fibre panels. These materials are on some occasions not well bonded and will release asbestos fibres if subject to abrasion and wear.

Bitumen felts and coatings may contain asbestos either bound in the bitumen matrix or as an asbestos paper liner. These materials are not likely to present a hazard during normal installation or use, but should be removed and disposed of in compliance with any regulation applicable.

Thermoplastic floor tiles can contain up to 25% asbestos usually chrysotile, PVC vinyl floor tiles and unbacked PVC flooring normally 7-10% chrysotile and asbestos paper backed PVC flooring the paper backing may contain up to 100% chrysotile. Fibre release is not normally an issue but may occur when the material is cut or subjected to abrasion.

**Textured coatings**. Decorative coatings on walls and ceilings usually contain 3-5% chrysotile. Fibre release may occur when subjected to abrasion.

Mastics, sealants, putties and floor tile adhesives may contain small amounts of asbestos. The only possible risk is from sanding of hardened material when appropriate precautions should be taken.

Reinforced plastic and resin composites, used for toilet cisterns, seats, banisters, stair nosings, window seals, lab bench tops, brake shoes and clutches in machines. The plastics usually contain 1-10% chrysotile and were used in for example car batteries to improve the acid resistance. Resins may contain between 20 and 50% amosite, but because of its composition fibre release is likely to be low.

ASBESTOS FIBRE TYPE COMMON NAMES		
Chrysotile	White Asbestos	
Amosite	Brown Asbestos	
Crocidolite	Blue Asbestos	
Fibrous Actinolite	N/A	
Fibrous Anthophyllite	N/A	
Fibrous Tremolite	N/A	



Chrysotile



Amosite



Crocidolite



Tremolite



Actinolite



Anthophyllite

# APPENDIX B RESULTS OF LABORATORY ANALYSIS

GRAIGUESWOOD, FRESHFORD, CO. KILKENNY



TEL: 056 8832414 FAX: 056 8832950 admin@phoenixenv.ie www.phoenixenv.ie

#### ASBESTOS BULK IDENTIFICATION REPORT

Report no: PE21-457	Date of Issue: 24th May 2021
I Neboli lio, I LZ I-431	Date of 133ue, 27 Iviav 2021

Client details:

Longford County Council, Aras an Chontae, Great Water Street, Longford

Identification of asbestos content of suspected asbestos containing material stated to have been sampled from the following location/site:

No. 24 Congress Terrace, Longford Town, Co. Longford

No of Samples received: 5 Date of receipt of samples: 21.5.2021 Date of analysis: 24.5.2021

Methodology. Analysis of samples received was carried out in accordance with HSE Method MDHS 77/HGS 248 and documented inhouse methods.

For samples received from the client and not sampled by Phoenix Environmental Safety Ltd.


This report is given in good faith on the basis of the samples and information received. Phoenix Environmental Safety Ltd. can take no responsibility for omissions, unrepresentative samples, inaccuracies or discrepancies in samples and information received.

#### **TEST RESULTS**

LAB. REF.	SAMPLE NO.	LOCATION	MATERIAL	ASBESTOS TYPE
S 01	PES 30357	Rear extension – Flat roof	Felt	No asbestos detected in sample
S 02	PES 30358	Ground floor WC	Toilet cistern	Amosite
S 03	PES 30359	Ground floor kitchen. Floor tile adhesive	Bitumen	Chrysotile
S 04	PES 30360	Ground floor, front room. Floor tile adhesive	Bitumen	Chrysotile
S 05	PES 30361	Ground floor, rear extension. Floor tile adhesive	Bitumen	No asbestos detected in sample
LABO	RATORY AN	ALYST Joh Hickory	DATE:	24 <sup>th</sup> May 2021
				-

## **APPENDIX C**

#### **ASBESTOS DATA SHEETS**

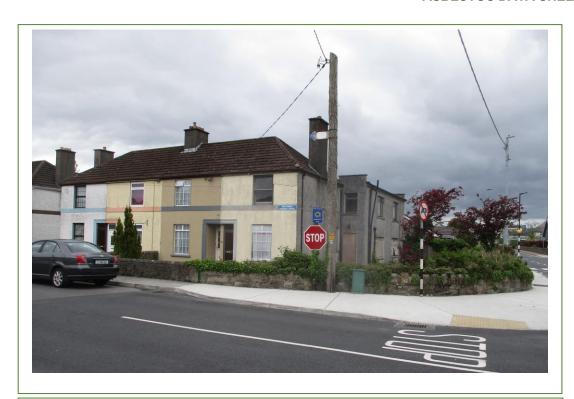

No. 24 Congress Terrace, Longford Town, Co. Longford



### PHOENIX ENVIRONMENTAL SAFETY LTD.

**ASBESTOS DATA SHEET** 



Created By

John Hickey

Date

25th May 2021

Site Details

No. 24 Congress Terrace, Longford Town,

Co. Longford

**Client Name** 

**Longford County Council** 

Survey Type

R/D Asbestos Survey

Site Ref

PE21-457

Building Ref.

No. 24 Congress Terrace

Material assessment score: N/A

Kitchen & front room

Location

Extent/ 35 m² approx.

Amount



Survey Date

21.5.2021

Sample No.

Priority assessment score: N/A

PES 30359

**Survey Company** 

Testing Laboratory. Phoenix Environmental Safety Ltd.

Phoenix Environmental Safety Ltd.

**MATERIAL ASSESSMENT** PRIORITY ASSESSMENT Product type Normal occupant activity Bitumen adhesive N/A Extent of damage Likelihood of disturbance N/A Well bound material N/A Surface treatment Human exposure potential Chrysotile N/A Asbestos type Maintenance activity

TOTAL SCORE: N/A

#### **CONCLUSIONS AND RECOMMENDATIONS**

The bitumen adhesive identified on the floor in the entrance, kitchen and front room contains Chrysotile (white) asbestos fibres. Bitumen adhesives contain a small quantity of asbestos fibres

As the floors are likely to be disturbed during the forthcoming refurbishment works, the asbestos containing bitumen adhesive should be removed by an asbestos asbestos removal contractor and disposed of as asbestos waste before the refurbishment works commence

See Appendix F for more details

All asbestos related works must be carried out in accordance with S.I. No. 386 of 2006 Safety, Health and Welfare at Work (Exposure to Asbestos) Regulations 2006-2010

## PHOENIX ENVIRONMENTAL SAFETY LTD.

**ASBESTOS DATA SHEET** 



Created By

John Hickey

Date

25th May 2021

Site Details

No. 24 Congress Terrace, Longford Town, Co. Longford

**Client Name** 

**Longford County Council** 

Survey Type

R/D Asbestos Survey

Site Ref

PE21-457

Building Ref.

No. 24 Congress Terrace

Ground floor W/C

Location

Extent/ 1 cistern Amount

Survey Date

21.5.2021

Sample No.

PES 30358

**Survey Company** 

Testing Laboratory.

Phoenix Environmental Safety Ltd.

Phoenix Environmental Safety Ltd.

	MATERIAL ASSESSMENT		PRIORITY ASSESSMENT
Product type	Resin toilet cistern	Normal occupant activity	N/A
Extent of damage	Low	Likelihood of disturbance	N/A
Surface treatment	Composite material	Human exposure potential	N/A
Asbestos type	Amosite	Maintenance activity	N/A
	Material assessment score: N/A	TOTAL SCORE: N/A	Priority assessment score: N/A

#### **CONCLUSIONS AND RECOMMENDATIONS**

The resin toilet cistern identified in the W/C on the ground floor contains Amosite (brown) asbestos fibres. Resin products may contain between 20 and 50% asbestos fibres

As the toilet is likely to be disturbed during the forthcoming refurbishment works, the asbestos containing resin toilet cistern should be removed by an asbestos asbestos removal contractor and disposed of as asbestos waste before the refurbishment works commence

See Appendix F for more details

All asbestos related works must be carried out in accordance with S.I. No. 386 of 2006 Safety, Health and Welfare at Work (Exposure to Asbestos) Regulations 2006-2010

## **APPENDIX D**

#### NON ASBESTOS CONTAINING MATERIALS



Concrete tiles on the roof of the house



Felt on the flat roof on the rear extension

#### NON ASBESTOS CONTAINING MATERIALS



Plasterboard on the ceilings



Polystyrene ceiling tiles

#### NON ASBESTOS CONTAINING MATERIALS



Woodchip paper on the kitchen ceiling



First floor sanitaryware

## **APPENDIX E**

#### NON ACCESSIBLE LOCATIONS

•	No inspection of live electrical or mechanical plant or similar requiring the attendance of a specialist engineer was carried out
•	No inspection of any areas requiring specialist access equipment other than a telescopic ladder was carried out
•	No underground services or confined spaces were inspected
•	All contractors working on the site should always remain vigilant to the possibility that concealed asbestos containing materials may be present on site. If any suspect asbestos containing materials are uncovered during the work, works must stop in that area and the suspect material should be sampled and analysed immediately for the presence of asbestos

## **APPENDIX F**

FLOOR PLANS & LOCATION OF ASBESTOS CONTAINING MATERIALS

Schematic diagram only Not to scale 25 <sup>th</sup> May 2021	No. 24 Congress Terrace, Longford Town, Co. Longford	
GROUND FLOOR PLAN		
Rear	xtension	
Thousand the second of the sec	ACOUNTY TO A COUNTY OF THE PARTY OF THE PART	
Adjacent properties		
Areas where asbestos containing bitumen adhesive was identified		
Area where an asbestos containing toilet cis	tern was identified	
